


ID	Task Mode	Task Name	Duration	Start	Finish	1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter			3rd Quarter								
						Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul	Sep	Nov	Jan	Mar	May	Jul		
0		Working Schedule	543 days?	Mon 4/6/15	Wed 5/3/17																								
1		1 New City Hall and Public Safety Campus P-SD	85 days	Mon 4/6/15	Fri 7/31/15																								
2		1.1 Visioning and information gathering	40 days	Mon 4/6/15	Fri 5/29/15																								
3		1.1.1 Kick-off Meeting	1 day	Tue 4/28/15	Tue 4/28/15																								
4		1.1.2 Peer Review (Boise)	1 day	Thu 5/14/15	Thu 5/14/15																								
5		1.1.3 Community Visioning	3 days	Wed 5/27/15	Fri 5/29/15																								
6		1.2 Programming	40 days	Mon 5/4/15	Fri 6/26/15																								
7		1.2.1 Program Meetings 1	3 days	Wed 5/27/15	Fri 5/29/15																								
8		1.2.2 Program Meetings 2	3 days	Wed 6/10/15	Fri 6/12/15																								
9		1.2.3 Program Meetings 3	3 days	Wed 6/24/15	Fri 6/26/15																								
10		1.3 Schematic Design	45 days	Mon 6/1/15	Fri 7/31/15																								
11		1.3.1 Steering Committee Meeting	3 days	Wed 6/24/15	Fri 6/26/15																								
12		1.3.2 Community Workshop	3 days	Wed 6/24/15	Fri 6/26/15																								
13		1.3.3 Steering Committee Meeting	1 day	Fri 7/31/15	Fri 7/31/15																								
14																													
15		2 New City Hall DD-CA	458 days	Mon 8/3/15	Wed 5/3/16																								
16		2.1 Design Development	45 days	Mon 8/3/15	Fri 10/2/15																								
17		2.2 Construction Documents	86 days	Mon 10/5/15	Mon 2/1/16																								
18		2.3 Agency Review and Permitting	30 days	Tue 2/2/16	Mon 3/14/16																								
19		2.4 Bidding (ideal Feb 1)	20 days	Tue 3/15/16	Mon 4/11/16																								
20		2.5 Construction Contracts/Approvals	15 days	Tue 4/12/16	Mon 5/2/16																								
21		2.6 Construction (tbd)	262 days	Tue 5/3/16	Wed 5/3/17																								
22		2.7 Early Demo/Site Construction (tbd)	171 days	Mon 9/7/15	Mon 5/2/16																								
23																													
24		3 Public Safety Campus DD-CA	239 days	Mon 8/3/15	Thu 6/30/16																								
25		3.1 Design Development	26 days	Mon 8/3/15	Mon 9/7/15																								
26		3.2 Construction Documents	45 days	Tue 9/8/15	Mon 11/9/15																								
27		3.3 Agency Review and Permitting	33 days	Tue 11/10/15	Thu 12/24/15																								
28		3.4 Bidding	21 days	Fri 1/1/16	Fri 1/29/16																								
29		3.5 Construction Contracts/Approvals	16 days	Mon 2/1/16	Mon 2/22/16																								
30		3.6 Phased construction (tbd)	93 days	Tue 2/23/16	Thu 6/30/16																								
31																													
32		4 CM/GC Selection	52 days?	Thu 5/21/15	Fri 7/31/15																								



Project: Working Schedule
Date: Fri 4/24/15

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

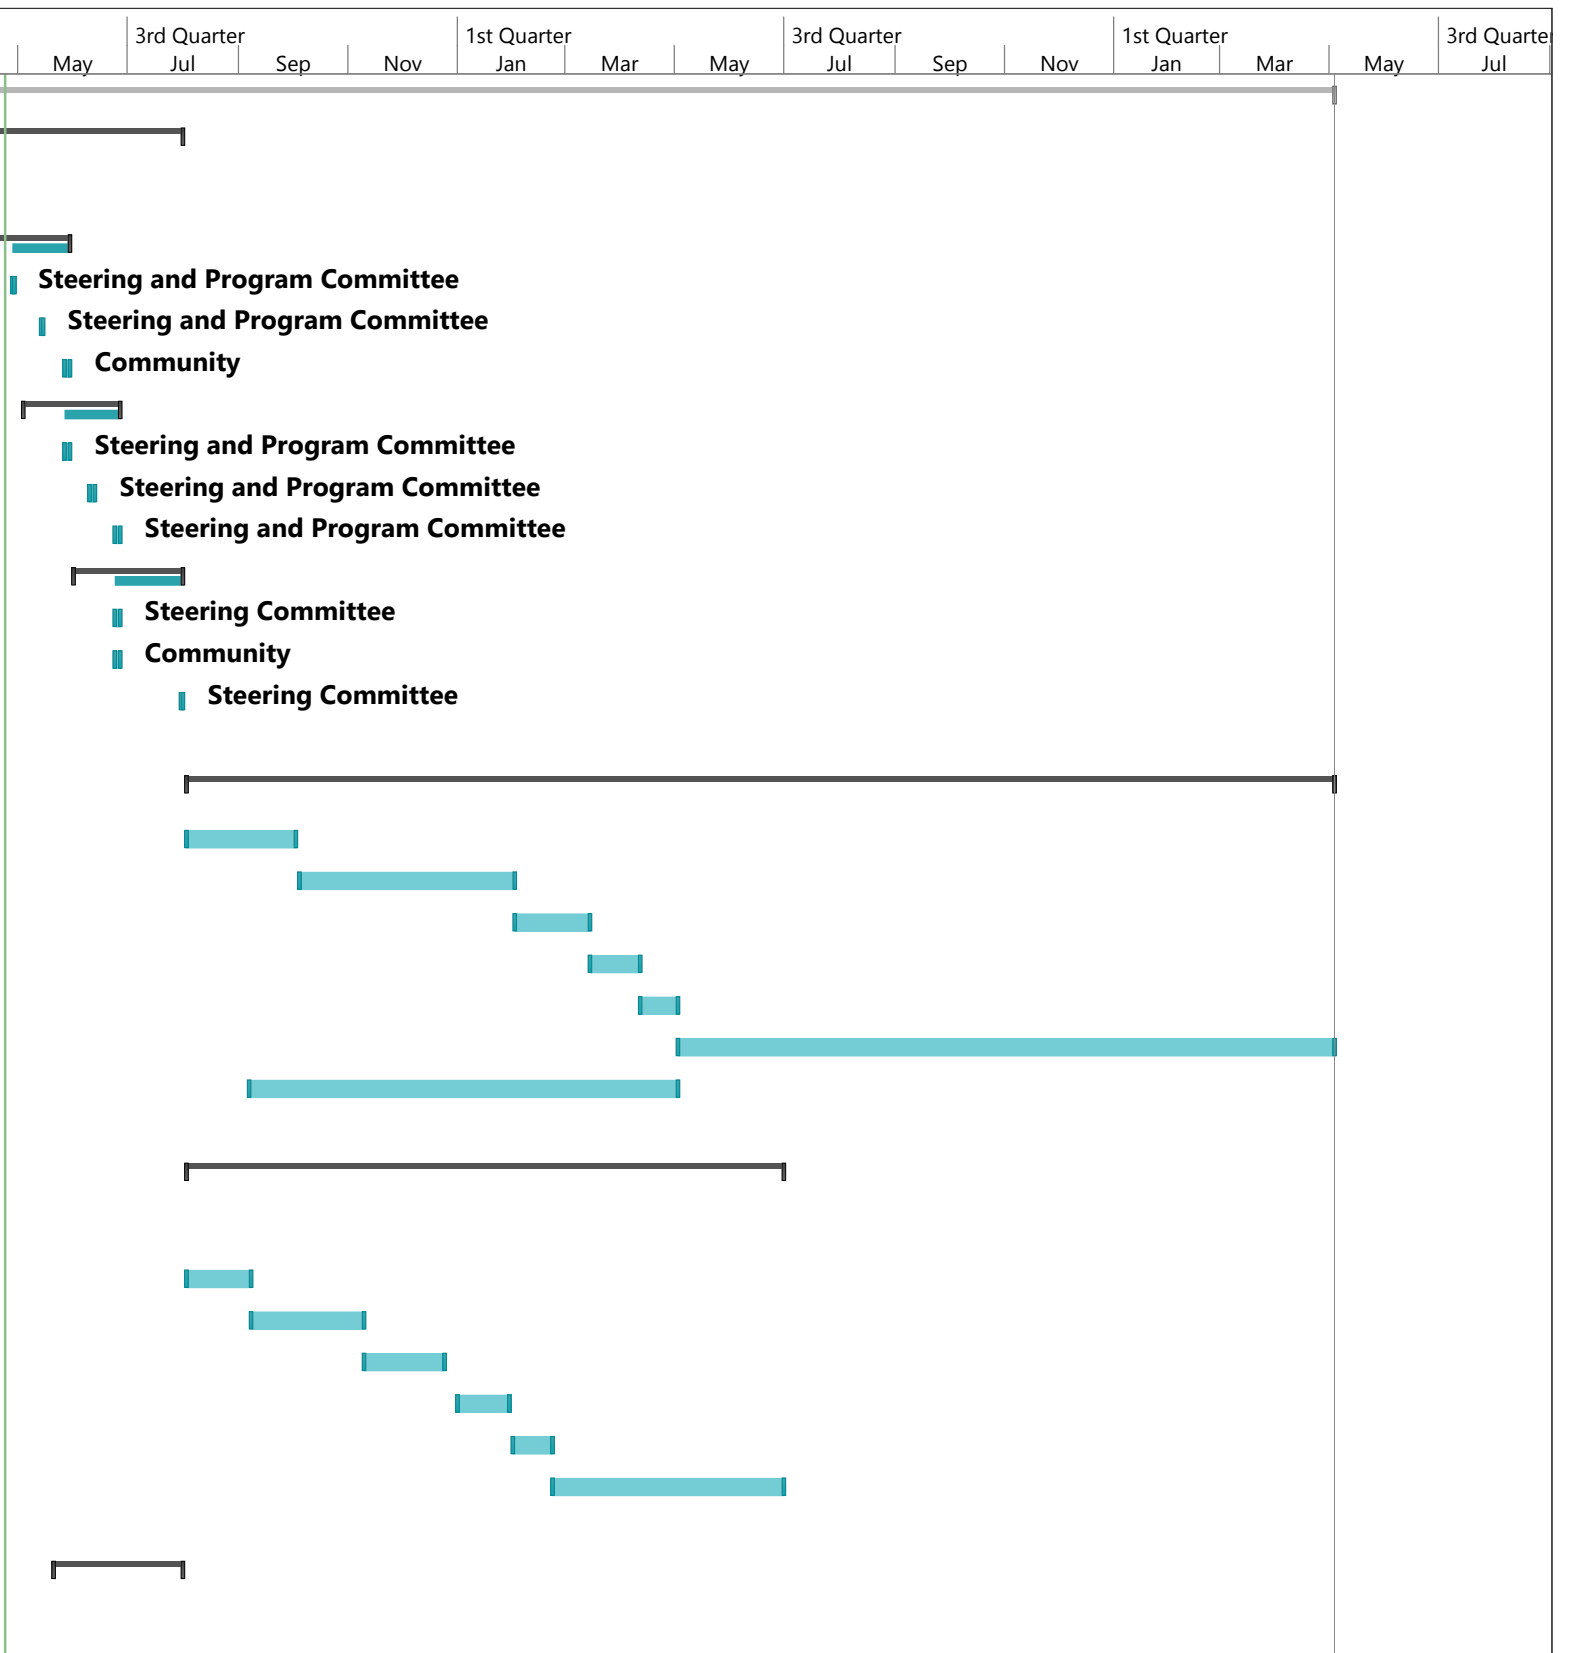
